


Benning RI/FS Project Schedule

ID	Task Name	Duration	Start	Finish	Q1 '16 Jan	Q2 '16 Apr	Q3 '16 Jul	Q4 '16 Oct	Q1 '17 Jan	Q2 '17 Apr	Q3 '17 Jul	Q4 '17 Oct	Q1 '18 Jan	Q2 '18 Apr	Q3 '18 Jul	Q4 '18 Oct
1	Response to Public Comments on the Draft RI Report	126 days	Tue 4/19/16	Tue 8/23/16												
6	Tech Memos and RI Work Plan Addendum #3 for Addl. Investigation	81 days	Fri 7/22/16	Tue 10/11/16												
17	Permitting	284 days	Thu 10/20/16	Mon 7/31/17												
19	Additional Field Investigation Activities	298 days	Mon 12/5/16	Fri 9/29/17												
20	Initial Mobilization	1 day	Mon 12/5/16	Tue 12/6/16												
21	Field Investigation Activities	297 days	Tue 12/6/16	Fri 9/29/17												
22	Finalize the RI Report	243 days	Fri 9/29/17	Wed 5/30/18												
23	Preapre Draft Final RI Report	119 days	Fri 9/29/17	Fri 1/26/18												
24	Draft Final RI Submittal	0 days	Fri 1/26/18	Fri 1/26/18												
25	DOEE Reviews	52 days	Fri 1/26/18	Mon 3/19/18												
26	Public Comment Period	30 days	Mon 3/19/18	Wed 4/18/18												
27	Finalize RI Report	42 days	Wed 4/18/18	Wed 5/30/18												
28	Final Submittal	0 days	Wed 5/30/18	Wed 5/30/18												
29	FS Report	305 days	Fri 9/29/17	Tue 7/31/18												
30	Draft FS Report Submittal	180 days	Fri 9/29/17	Wed 3/28/18												
31	DOEE Reviews	50 days	Wed 3/28/18	Thu 5/17/18												
32	Public Comment Period	30 days	Thu 5/17/18	Sat 6/16/18												
33	Finalize FS Report	45 days	Sat 6/16/18	Tue 7/31/18												
34	Final Submittal	0 days	Tue 7/31/18	Tue 7/31/18												
35	*** Assumptions are listed below.															

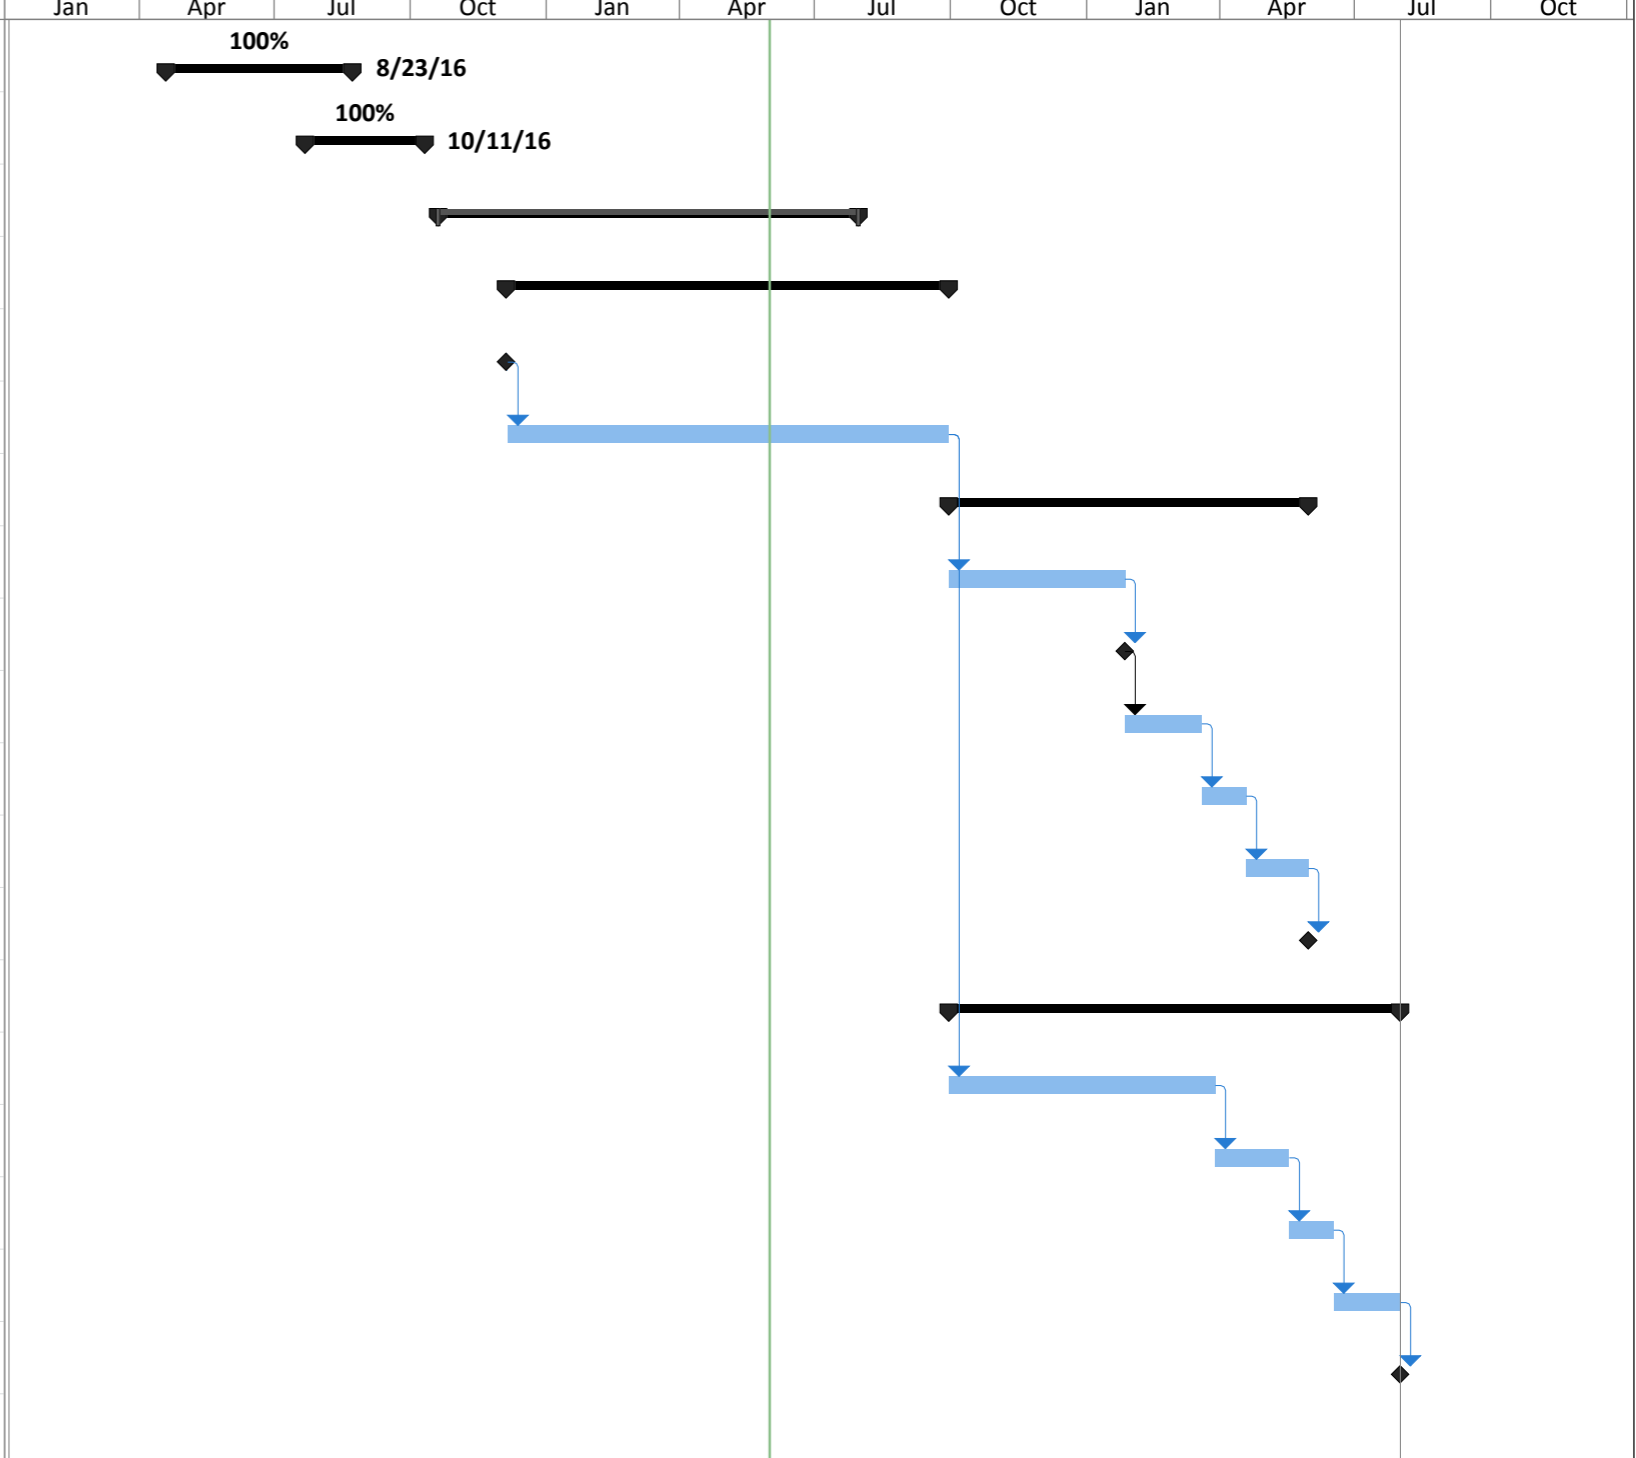

Date: Thu 6/1/17	Task Project Summary Split External Tasks Milestone External Milestone Summary Inactive Task	Inactive Milestone Inactive Summary Manual Task Duration-only 	Manual Summary Rollup Manual Summary Start-only Finish-only 	Deadline Progress Manual Progress 	▼
------------------	---	--	--	---	---

Benning RI/FS Project Schedule

35 * Assumptions are listed below.**

The schedule is based on the following assumptions:

1. All task durations are in calendar days.
2. The schedule shows assumed timeframes for DOEE's document reviews. One Draft and one Final submission are assumed for each document. If additional reviews or longer review times are needed, the schedule needs to be adjusted accordingly.
3. As of the revision of this calendar, DOEE is reviewing data collected thus far and requiring additional work. This will require permit modifications or additional permits.
4. Permits (Task 17) include outstanding permits as well as additional permits to be applied for based on #3 above. Schedule will be revisited upon receipt of all permits and access agreements.
5. Duration of additional field investigation activities (Task 19) is currently an estimate and dependent upon the extent of additional work required and the receipt of permits.
6. Duration for data validation and compilation, as part of the field activities (Task 21), is based on a laboratory turnaround time of 28 days. Data validation and compilation for forensics and some specialized analyses could take longer.
7. Task 25 - Draft-Final RI Report Submittal schedule is within the Consent Decree (CD) requirements.
8. Task 31 - Draft FS Report Submittal schedule is within the CD requirements.
9. This schedule assumes that treatability studies are not necessary prior to completing the FS. In the event a treatability study is required, this schedule for the FS Report will be revised as needed and the Final FS shall be approved by September 30, 2018.
